

ALL VEHICLE AND  
PEDESTRIAN ROUTES  
OPEN TO TRAFFIC

**LEGEND**  
 — WORK DONE THIS STAGE  
 — WORK DONE PREVIOUS STAGE




**HURON PARKWAY – NIXON ROAD  
IMPROVEMENT PROJECTS**

- STAGE 5 CONSTRUCTION**
- HURON PARKWAY (WEST LEG)
    - OPEN TO TRAFFIC WITH FLAG CONTROL
    - PLACEMENT OF TOP LAYER OF ASPHALT
  - HURON PARKWAY (EAST LEG)
    - OPEN TO TRAFFIC WITH FLAG CONTROL
    - PLACEMENT OF TOP LAYER OF ASPHALT
  - NIXON ROAD (NORTH LEG)
    - OPEN TO TRAFFIC WITH FLAG CONTROL
    - PLACEMENT OF TOP LAYER OF ASPHALT
  - NIXON ROAD (SOUTH LEG)
    - OPEN TO TRAFFIC WITH FLAG CONTROL
    - PLACEMENT OF TOP LAYER OF ASPHALT
  - FRONTAGE ROAD (FOR NIXON ROAD)
    - OPEN TO TRAFFIC WITH FLAG CONTROL
    - PLACEMENT OF TOP LAYER OF ASPHALT

# HURON PARKWAY - NIXON RD. TEMPORARY TRAFFIC CONTROL PLAN

## STAGE 5 OF 5 - FINAL PAVING DAY

ALTERNATIVE 2: WEATHER PERMITTING, ONE DAY DURING WEEK OF JUNE 22, 2009

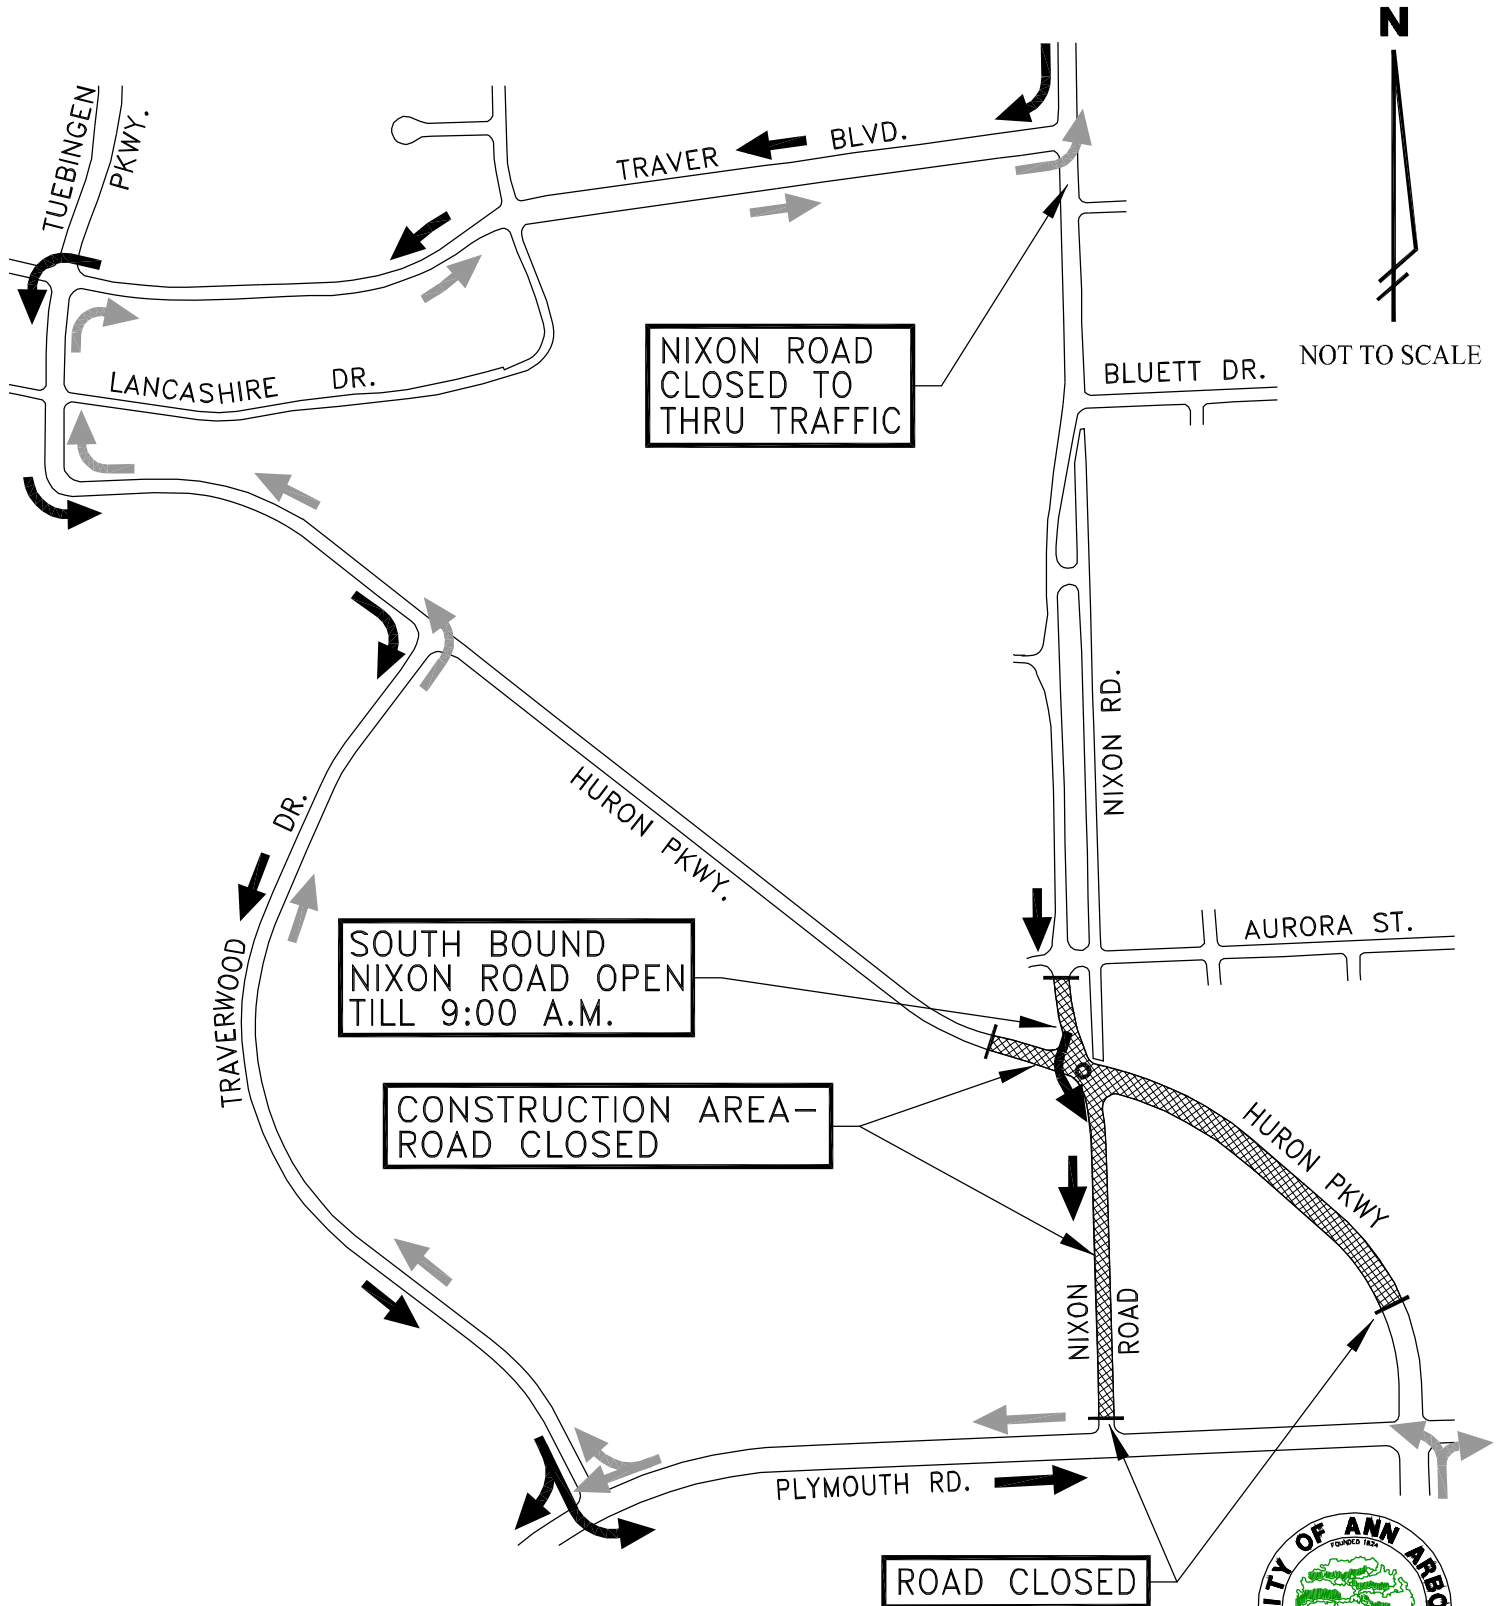



**CITY OF ANN ARBOR**  
PROJECT MANAGEMENT SERVICES UNIT  
100 NORTH FIFTH AVE. P.O. BOX 8647  
ANN ARBOR, MICHIGAN 48107-8647  
WWW.A2GOV.ORG  
(734) 794-6410

For Immediate Release  
June 16, 2009

Homayoon Pirooz, P.E., Manager  
hpirooz@a2gov.org  
734-794-6411

**Notice of Temporary Traffic Control Plan**  
**HURON PARKWAY-NIXON ROAD IMPROVEMENT PROJECT**  
**Construction Stage 5 of 5 - June 22, 2009**

**Location and Limits of Affected Area:**

Nixon Road from the intersection of Plymouth Road to the intersection of Aurora Street. Huron Parkway from the intersection of Plymouth Road to the intersection of Traver Wood Dr

**Description of Construction:**

At this stage of the project the contractor will complete the final paving of the new roundabout, Huron Parkway and Nixon Road. The entire paving operation will be completed in one day. During this operation the intersection of Huron Parkway and Nixon Road will be closed to all traffic. This stage of construction is highly weather – dependant. It is our intent to complete this work on a dry day beginning Saturday June 20, 2009.

**Temporary Construction Traffic Control Plan if the work take place on Saturday June 20, or Sunday June 21, 2009:**

- The intersection of Nixon Road and Huron Parkway will be closed to all traffic during the paving operation.
- The through traffic will use the posted detour route from the intersection of Plymouth Road and Traverwood Dr to the intersection of Nixon Road and Traver Road Blvd (map attached).
- The local traffic will be maintained, but will be not permitted to enter the roundabout.

**Temporary Construction Traffic Control Plan for Stage 5 if the work to take place on a weekday during the week of June 22, 2009:**

- Prior to 9:00 a.m. the SB traffic on Nixon Road will be maintained, but the road will be closed off to the NB traffic.
- After 9:00 a.m. the intersection of Nixon Road and Huron Parkway will be closed to all traffic.
- The through traffic will use the posted detour route from the intersection of Plymouth Road and Traverwood Dr, to the intersection of Nixon Road and Traver Road Blvd (map attached).
- The local traffic will be maintained, but will be not permitted to enter the roundabout

Pedestrian traffic on the sidewalks will be maintained. During this construction the traffic may experience brief delays within the areas influenced by this work. Detour signs will be posted for this construction; however the motorists are advised to seek alternate routes. To maintain the safety of all, please reduce speeds and drive cautiously through work zones. We thank you in advance for your patience as these necessary public infrastructure improvements are completed.

**Project Contacts:**

City of Ann Arbor

Igor V. Kotlyar, P.E., Senior Project Engineer, (734) 794-6410 x43634

David Clemons, Construction Supervision, (734) 323-7942

Orchard, Hiltz & McCliment, Inc.

Andrew A. Konyha, Civil Engineer, (734) 891-2448

Pamar Construction Company

Steve Brown, Construction Contractor, (586) 405-2391
